Alaska Department of Fish and Game Wildlife Restoration Grant

GRANT NUMBER: AKW-D-8-2021

PROJECT NUMBER: Project 1.0

PROJECT TITLE: Oliver Inlet Access Improvements

PERIOD OF PERFORMANCE: March 1, 2021–December 31, 2022

PERFORMANCE YEAR: March 1, 2021–September 30, 2021

REPORT DUE DATE: December 29, 2021

PRINCIPAL INVESTIGATOR:

Katie Sechrist

ADF&G, Division of Wildlife Conservation

333 Raspberry Road Anchorage, AK

Phone: (907) 267-2541

Email: katie.sechrist@alaska.gov

COOPERATORS:

Rys Miranda, P.E.

DNR, Division of Parks and Outdoor Recreation

550 W. 7th Avenue, Suite 1340 Anchorage, Alaska 99501 Phone: (907) 269-8736

E-Mail: rys.miranda@alaska.gov

Authorities: 2 CFR 200.328

2 CFR 200.301 50 CFR 80.90

I. PROGRESS ON PROJECT OBJECTIVES DURING PERFORMANCE YEAR

OBJECTIVE 1: To repair/restore ~ 500 feet of the existing Oliver Inlet tram to improve safety and hunter access.

ACCOMPLISHMENTS: The funding structure for this project was established in June 2021. Work commenced shortly after and included reconnaissance and field data collection work performed on June 22 and September 1, 2021, respectively. Base mapping for design work was completed during this performance period.

II. SUMMARY OF WORK COMPLETED ON PROJECT TO DATE

Milestones completed to date include establishing the project budget structure, reconnaissance and field survey, and development of the project base map for design work.

III. SIGNIFICANT DEVELOPMENT REPORTS AND/OR AMENDMENTS

N/A.

Financial Summary:

Non-Federal Match

Financial Coding IRIS AR/Task	Starting Amount	Amount Spent	Remaining Balance
107039199 / 79CB	\$21,188.91	\$6,347.54	\$14,841.37
107820011 / 10PKSF82M2	\$6,000.00	\$0.00	\$6,000.00

Grant Funds

Financial Coding IRIS AR/Program	Starting Amount	Amount Spent	Remaining Balance
10RS71037 / 10PKSF0082	\$ 64,575.00	\$0.00	\$64,575.00

IV. PUBLICATIONS



Figure 1.—Park entrance and beginning of Oliver Inlet tram.

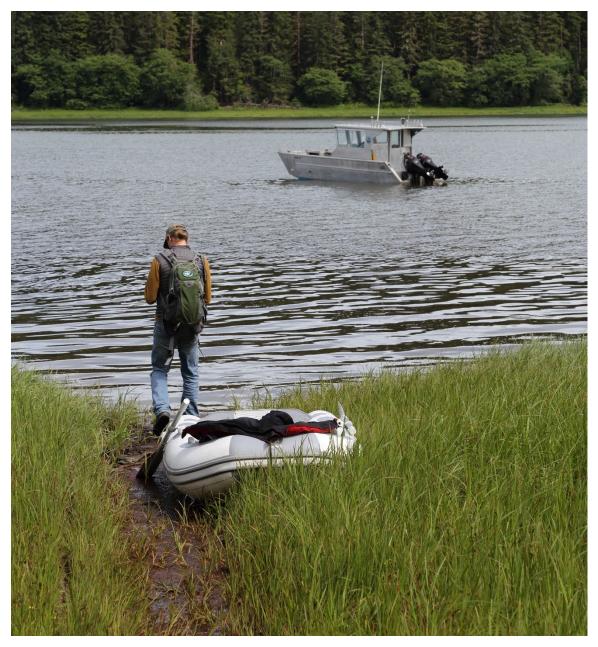


Figure 2.—Beach access to Oliver Inlet.

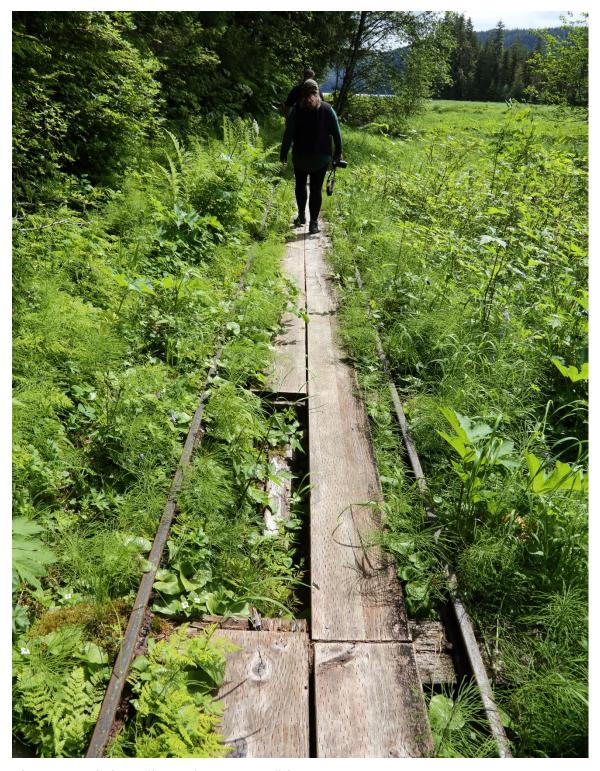


Figure 3.—Existing Oliver Inlet tram conditions.



Figure 4.—Existing conditions at Seymour Canal terminal and tram cart.

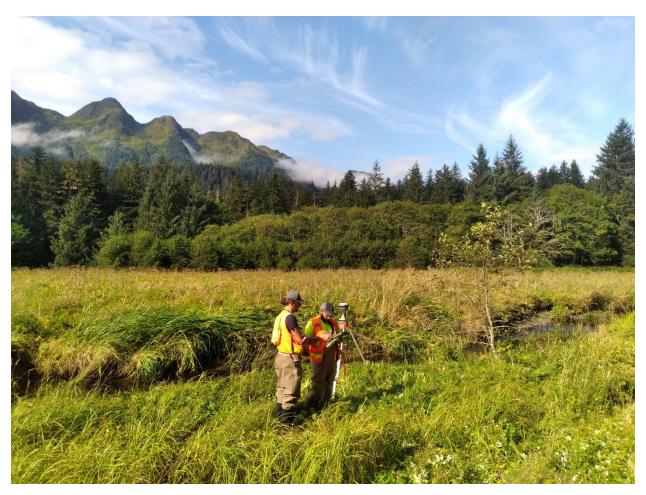


Figure 5.-Survey work taking place.

V. RECOMMENDATIONS FOR THIS PROJECT

The project will continue as planned with design beginning in December 2021 and construction is anticipated to take place summer 2022. No additional changes are recommended or anticipated at this time.

Prepared by:

Rys Miranda, DNR, Division of Parks and Outdoor Recreation

Katie Sechrist, ADF&G, Division of Wildlife Conservation, Hunter Access Program

Date: 12/9/2021
